






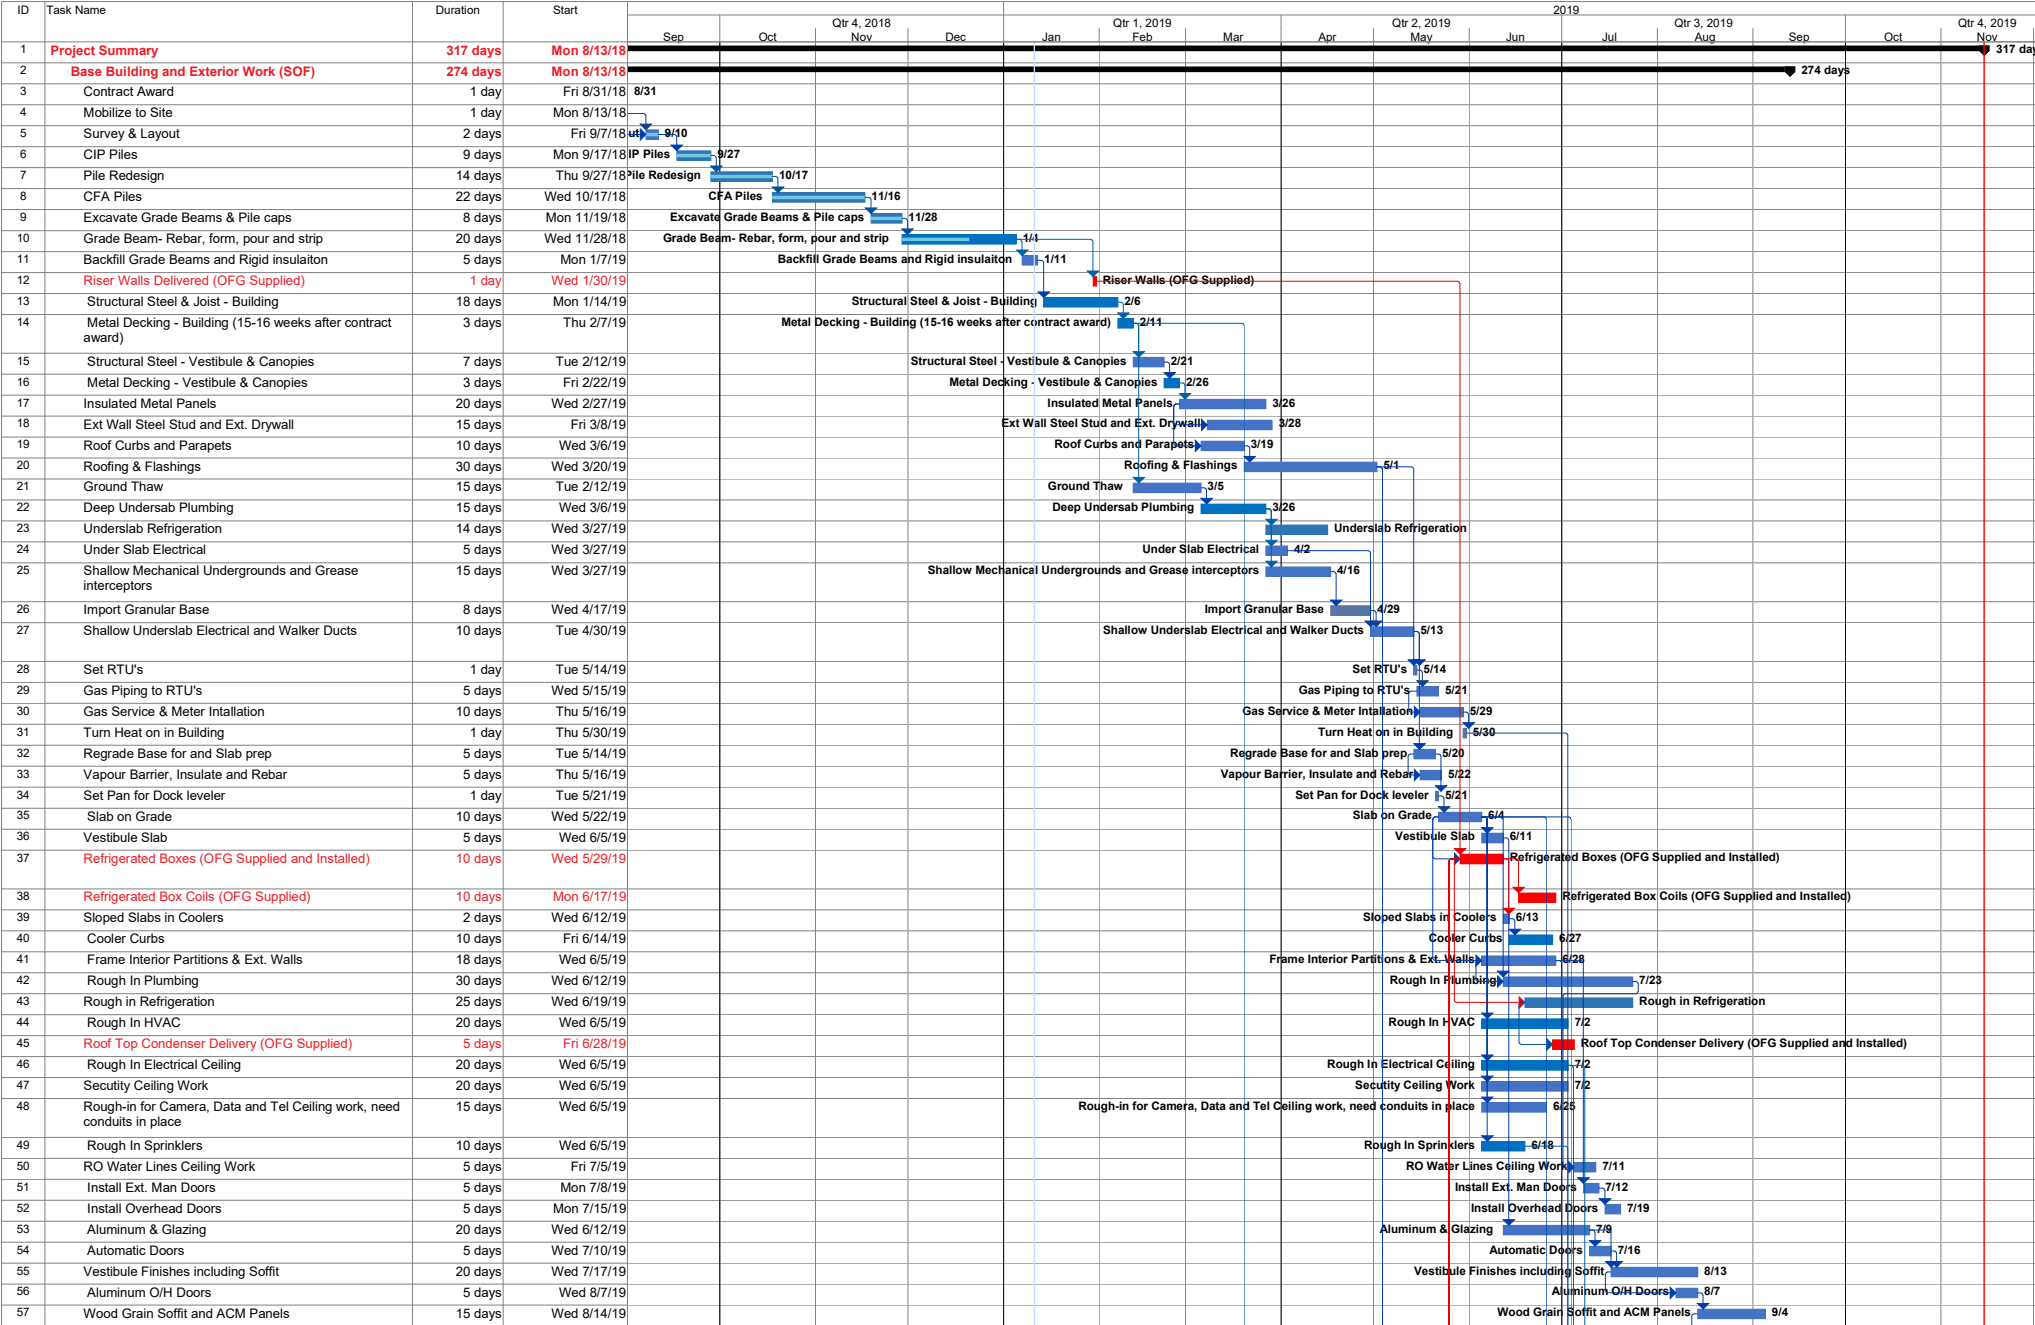

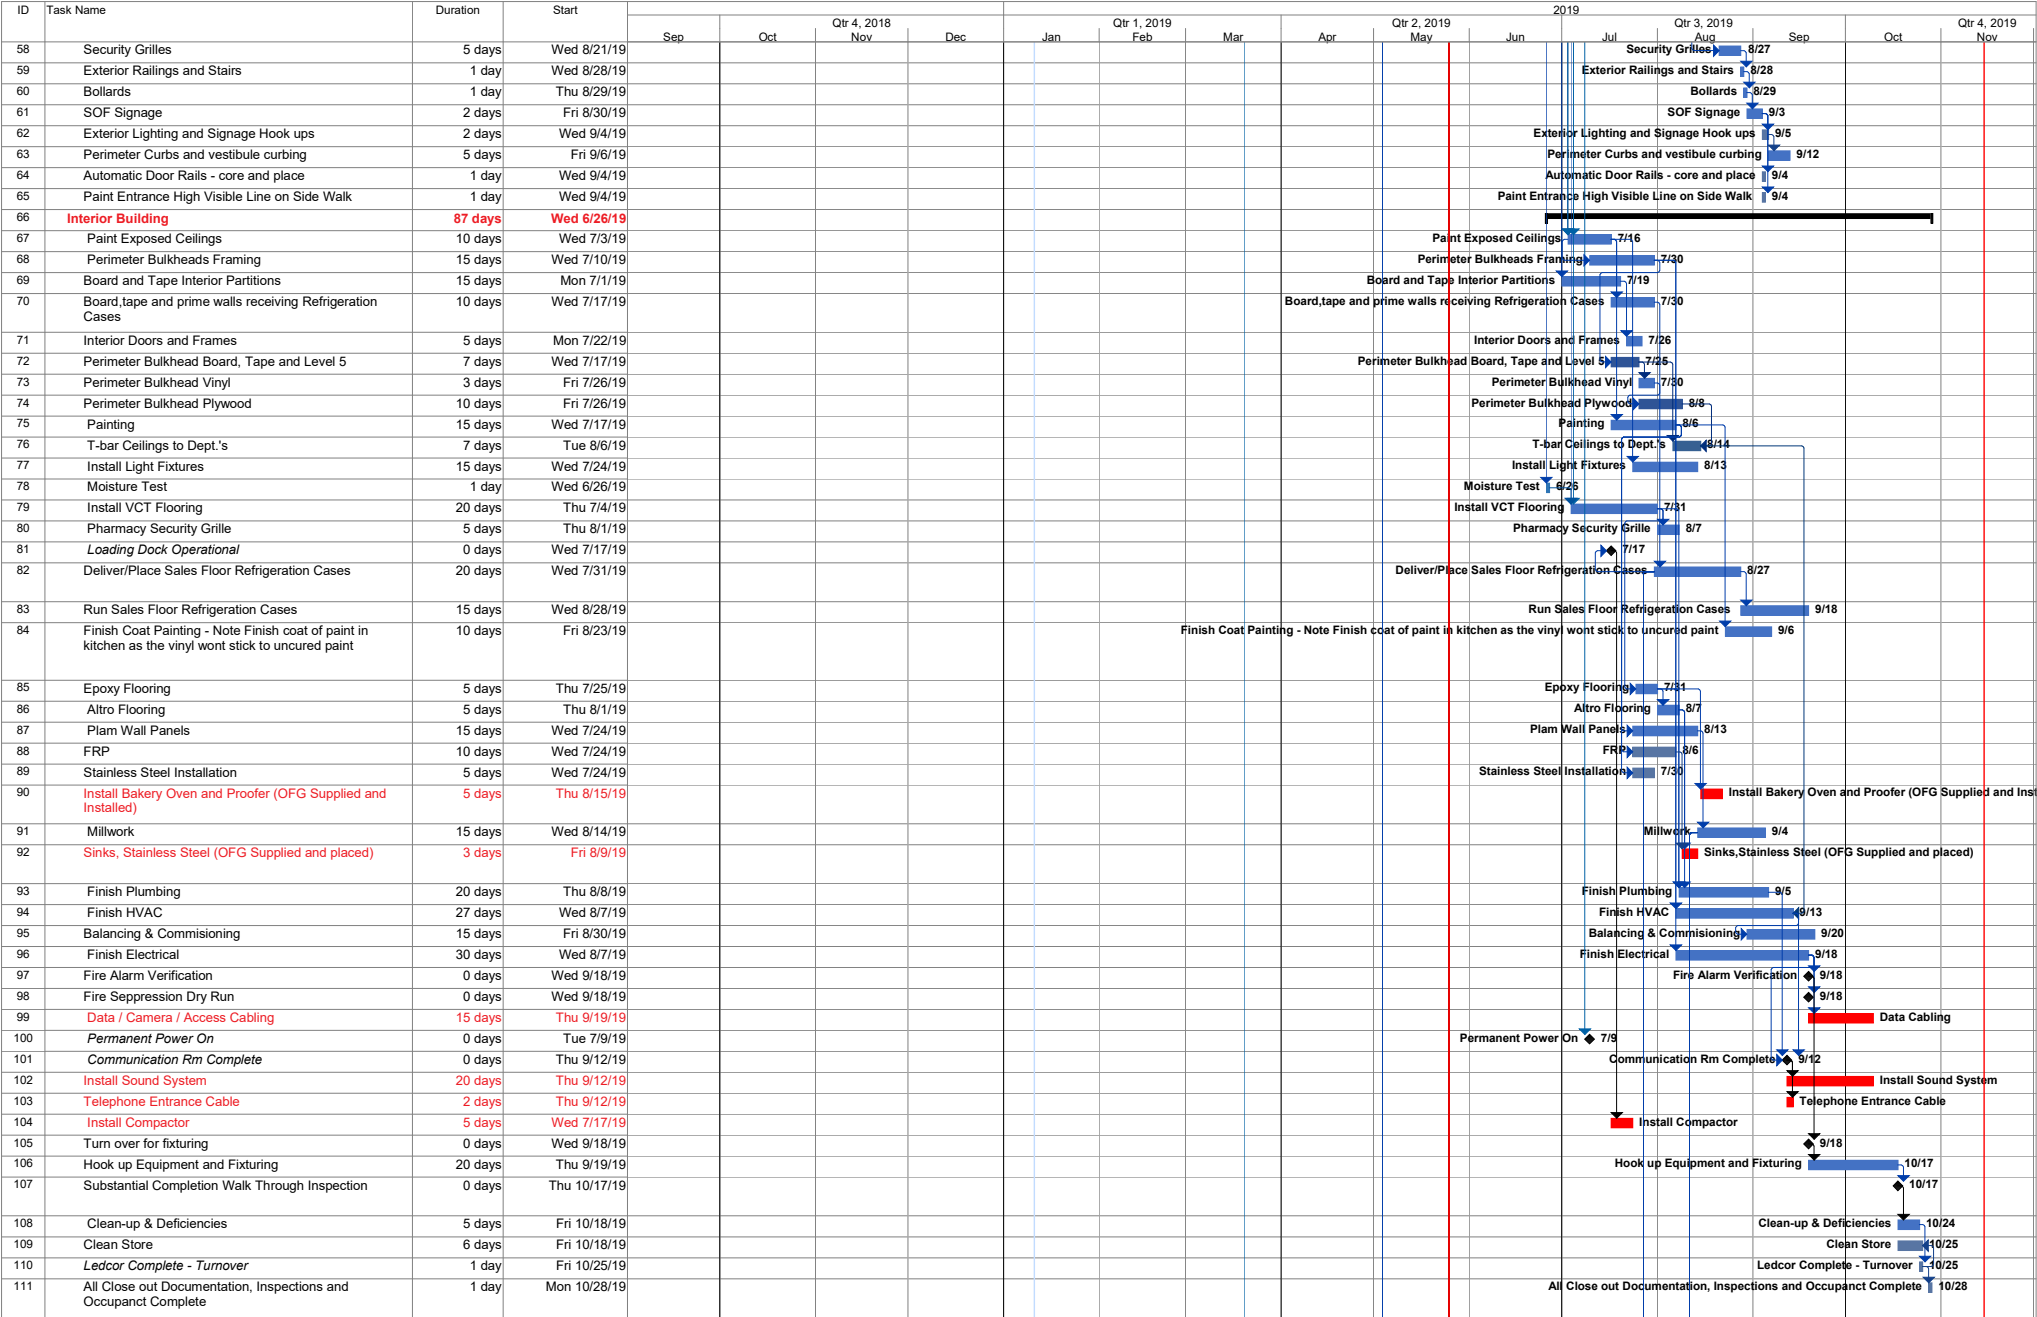

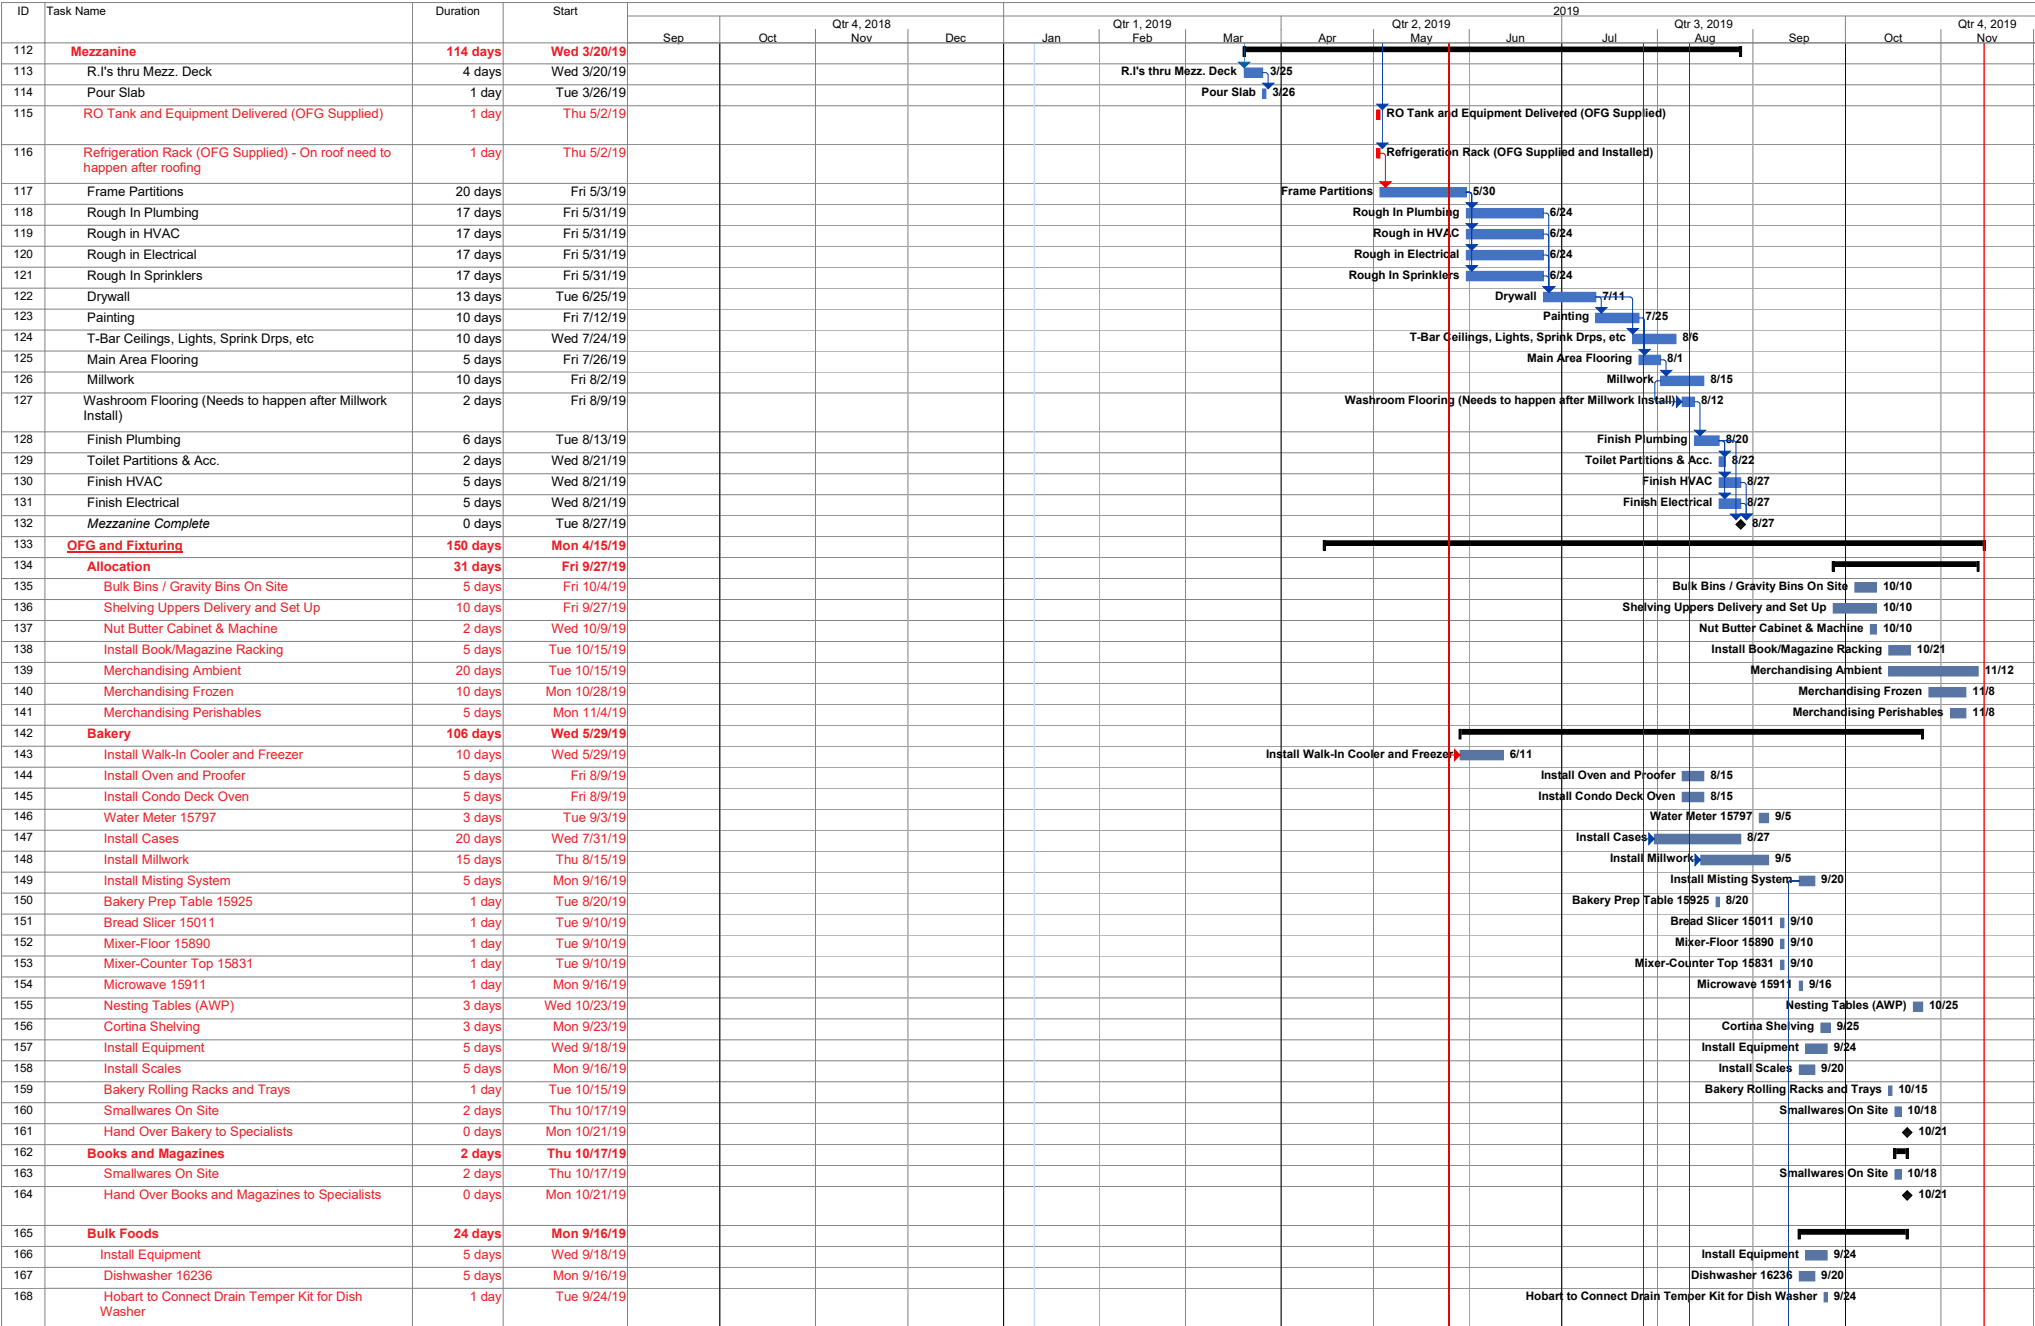

Task Name	Duration	Start	Qtr 4, 2018				Qtr 1, 2019			Qtr 2, 2019		2019		Qtr 3, 2019		Qtr 4, 2019	
			Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov
169	Smallwares On Site	2 days				Thu 10/17/19											
170	Hand Over Bulk Foods to Specialists	0 days				Mon 10/21/19											
171	Dairy	82 days				Wed 5/29/19											10/21
172	Install Walk-In Cooler	10 days				Wed 5/29/19											
173	Walk-In Cooler Glass Doors and Frame	3 days				Tue 6/4/19											
174	Install Glass Door Dairy Cases	20 days				Wed 7/31/19											
175	Smallwares On Site	2 days				Tue 9/17/19											
176	Hand Over Dairy to Specialists	0 days				Sat 9/21/19											
177	Deli	101 days				Wed 5/29/19											
178	Install Walk-In Cooler	10 days				Wed 5/29/19											
179	Install Cases	20 days				Wed 7/31/19											
180	Install Millwork	15 days				Thu 8/15/19											
181	Sliding Scale Stands 25514	1 day				Mon 8/26/19											
182	Install Misting System	5 days				Mon 9/16/19											
183	Slicer 25786	1 day				Tue 9/24/19											
184	Slicer Auto 25787	1 day				Tue 9/24/19											
185	Install Equipment	5 days				Wed 9/18/19											
186	Install Scales	5 days				Mon 9/16/19											
187	Smallwares On Site	2 days				Thu 10/17/19											
188	Hand Over Deli to Specialists	0 days				Mon 10/21/19											
189	E-Comm	56 days				Wed 7/31/19											
190	Install Glass Door Coolers / Freezer	20 days				Wed 7/31/19											
191	Install Millwork	15 days				Thu 8/15/19											
192	Install Equipment	5 days				Wed 9/18/19											
193	Smallwares on Site	2 days				Thu 10/17/19											
194	Hand Over E-Comm Department to Specialists	0 days				Mon 10/21/19											
195	Fish	101 days				Wed 5/29/19											
196	Install Walk-In Cooler	10 days				Wed 5/29/19											
197	Install Service Cases	20 days				Wed 7/31/19											
198	Install Fish Millwork	15 days				Thu 8/15/19											
199	Install Misting System	5 days				Mon 9/16/19											
200	Install Equipment	5 days				Wed 9/18/19											
201	Install Scales	5 days				Mon 9/16/19											
202	Smallwares On Site	2 days				Thu 10/17/19											
203	Hand Over Fish Department to Specialists	0 days				Mon 10/21/19											
204	Floral	59 days				Wed 7/31/19											
205	Install Refrigerated Cases	20 days				Wed 7/31/19											
206	Install Floral Millwork	15 days				Thu 8/15/19											
207	Install Equipment	5 days				Wed 9/18/19											
208	Floral Display Tables (AWP)	1 day				Wed 10/23/19											
209	Smallwares On Site	2 days				Thu 10/17/19											
210	Hand Over Floral Department to Specialists	0 days				Mon 10/21/19											
211	Food Service	110 days				Wed 5/29/19											
212	Install Chicken Cooler	10 days				Wed 5/29/19											
213	Install Refrigerated / Hot Cases	20 days				Wed 7/31/19											
214	Install Millwork	15 days				Thu 8/15/19											
215	Rotisserie 27624	1 day				Tue 8/27/19											
216	Combi Oven 27847	1 day				Wed 9/11/19											
217	3dr Upright Freezer 27476	1 day				Wed 9/11/19											
218	Hot Holding Cabinet 27890	1 day				Wed 10/2/19											
219	Jones Soda Machine / Stand / Rack / Ice Cuber	3 days				Tue 10/29/19											
220	Dishwasher/Pot Washer 27937	5 days				Mon 9/16/19											
221	Hobart to Connect Drain Temper Kit for Pot Washer	1 day				Tue 9/24/19											
222	Hobart to Commission Pot Washer	1 day				Tue 9/24/19											
223	Install Misting System	5 days				Mon 9/16/19											
224	Install Equipment	5 days				Wed 9/18/19											
225	Install Scales	5 days				Mon 9/16/19											



Task Name	Duration	Start	Qtr 4, 2018				Qtr 1, 2019			Qtr 2, 2019			2019		Qtr 3, 2019		Qtr 4, 2019	
			Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	
226	Smallwares On Site	2 days																
227	Hand Over Fast Foods to Specialists	0 days																
228	Front End Operations	63 days																
229	Communication Room Complete	1 day																
230	Data / Access / Camera / Security Cabeling	20 days																
231	IT DATA Rack	1 day																
232	Safe Install Cash Office	1 day																
233	General Offices Complete	1 day																
234	Hand Over Offices	0 days																
235	Install Customer Service Millwork	15 days																
236	Install Lottery	2 days																
237	Install Checkstands	3 days																
238	Install Registers	5 days																
239	Install Self-Scan Checkouts	5 days																
240	Smallwares On Site	2 days																
241	Hand Over Front End to Specialists	0 days																
242	Frozen Foods	101 days																
243	Install Grocery Freezer	10 days																
244	Install Glass Door Freezers	20 days																
245	Smallwares On Site	2 days																
246	Hand Over Frozen Foods to Specialists	0 days																
247	Meat	101 days																
248	Install Walk-In Cooler / Cutting Room	10 days																
249	Install Glass Door Frozen Cases	20 days																
250	Install Fresh Cases	20 days																
251	Install Service Cases	20 days																
252	Install Open Frozen Cases	20 days																
253	Install Stainless Steel Uppers	3 days																
254	Install Misting System	5 days																
255	Install Equipment	5 days																
256	Install Scales	5 days																
257	Smallwares On Site	2 days																
258	Hand Over Meat to Specialists	0 days																
259	Pharmacy	45 days																
260	Install Millwork	15 days																
261	Safe Install	1 day																
262	Install Equipment	5 days																
263	Smallwares On Site	2 days																
264	Hand Over Dispensary to Specialists	0 days																
265	Hand Over OTC to Specialists	0 days																
266	Hand Over Haba to Specialists	0 days																
267	Produce	101 days																
268	Install Walk-In Cooler	10 days																
269	Install Cases	20 days																
270	Heat Exchanger	1 day																
271	Install Backroom Equipment	3 days																
272	Install Dry Tables	1 day																
273	Install Misting System	5 days																
274	Smallwares On Site	2 days																
275	Hand Over Produce to Specialists	0 days																
276	Starbucks	0 days																
277	Install Kiosk / OTG	0 days																
278	Final Hook Up Power / Plumbing	0 days																
279	Espresso Machine 29005	0 days																
280	Install Equipment	0 days																
281	Smallwares On Site	0 days																
282	Handover Starbucks to Specialists	0 days																
283	Facilities Maintenance Support Work	38 days																
284	Jan / San Suplies On Site	1 day																
285	Sanitation Equipment Installation	3 days																



ID	Task Name	Duration	Start	2019												2019
				Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	
286	Prelim Facilities Maintenance Inspection	2 days	Mon 10/7/19													Prelim Facilities Maintenance Inspection █ 10/8
287	Janitorial	20 days	Tue 10/15/19													Janitorial █ 11/12
288	Facilities Maintenance Inspection	2 days	Wed 11/6/19													Facilities Maintenance Inspection █ 11/7
289	Head Office Support Activities	80 days	Mon 7/22/19													
290	Bakery Merchandising Setup	15 days	Mon 10/21/19													Bakery Merchandising Setup █ 11/8
291	Books and Magazines Merchandising Setup	15 days	Mon 10/21/19													Books and Magazines Merchandising Setup █ 11/8
292	Bulk Merchandising Setup	15 days	Mon 10/21/19													Bulk Merchandising Setup █ 11/8
293	Dairy Merchandising Setup	15 days	Mon 10/21/19													Dairy Merchandising Setup █ 11/8
294	Deli Merchandising Setup	15 days	Mon 10/21/19													Deli Merchandising Setup █ 11/8
295	E-Comm Merchandising Setup	15 days	Mon 10/21/19													E-Comm Merchandising Setup █ 11/8
296	Fast Food Merchandising Setup	15 days	Mon 10/21/19													Fast Food Merchandising Setup █ 11/8
297	Fish Merchandising Setup	15 days	Mon 10/21/19													Fish Merchandising Setup █ 11/8
298	Floral Merchandising Setup	15 days	Mon 10/21/19													Floral Merchandising Setup █ 11/8
299	Front End Merchandising Setup	15 days	Mon 10/21/19													Front End Merchandising Setup █ 11/8
300	Frozen Merchandising Setup	15 days	Mon 10/21/19													Frozen Merchandising Setup █ 11/8
301	IT Support Work	35 days	Mon 9/23/19													IT Support Work █ 11/12
302	Lottery Merchandising Setup	5 days	Mon 11/4/19													Lottery Merchandising Setup █ 11/8
303	Marketing Support Work	80 days	Mon 7/22/19													Marketing Support Work █ 11/13
304	Meat Merchandising Setup	15 days	Mon 10/21/19													Meat Merchandising Setup █ 11/8
305	Merchandising Support Work (Labels)	25 days	Mon 10/7/19													Merchandising Support Work (Labels) █ 11/12
306	Pharmacy Merchandising Setup	15 days	Mon 10/21/19													Pharmacy Merchandising Setup █ 11/8
307	Produce merchandising Setup	15 days	Mon 10/21/19													Produce merchandising Setup █ 11/8
308	Product Integrity Work	3 days	Wed 10/9/19													
309	Preliminary Health Inspection and Deficiency Repairs	3 days	Wed 10/9/19													Preliminary Health Inspection and Deficiency Repairs █ 10/11
310	Final Health Inspection	1 day	Fri 10/11/19													Final Health Inspection █ 10/11
311	Resource Protection Work	150 days	Mon 4/15/19													
312	Cameras and Access Control	20 days	Tue 9/3/19													Cameras and Access Control █ 9/30
313	Intrusion Alarm Installation	3 days	Tue 8/27/19													Intrusion Alarm Installation █ 8/29
314	Security Guards	150 days	Mon 4/15/19													Security Guards █ 11/14
315	Sign-in	21 days	Fri 10/11/19													Sign-in █ 11/12
316	ULC Monitoring	0 days	Fri 11/8/19													◆ 11/8
317	Receiving Clerk On Site	60 days	Mon 8/19/19													Receiving Clerk On Site █ 11/13
318	Fixture Installer Onsite	50 days	Tue 9/3/19													Fixture Installer Onsite █ 11/13
319	Refrigeration Start Up	15 days	Mon 9/23/19													Refrigeration Start Up █ 10/11
320	Pallet Jacks	1 day	Wed 8/28/19													Pallet Jacks █ 8/28
321	Wheelers	1 day	Wed 10/9/19													Wheelers █ 10/9
322	Compactor and Bailer Install.	5 days	Mon 9/23/19													Compactor and Bailer Install. █ 9/27
323	Shelving Base Decks / Up-rights Delivery and Set Up	5 days	Tue 9/3/19													Shelving Base Decks / Up-rights Delivery and Set Up █ 9/9
324	Versa Ends / RX Shelving Delivery and Set Up	5 days	Mon 9/9/19													Versa Ends / RX Shelving Delivery and Set Up █ 9/13
325	Department Signage	5 days	Mon 9/23/19													Department Signage █ 9/27
326	C2 Hanging Signage	2 days	Mon 9/16/19													C2 Hanging Signage █ 9/17
327	C2 installer and Low Signage	5 days	Mon 9/30/19													C2 installer and Low Signage █ 10/4
328	Exterior Signage	5 days	Mon 9/9/19													Exterior Signage █ 9/13
329	Fire Safety Plan	1 day	Tue 9/24/19													Fire Safety Plan █ 9/24
330	First Aid Kit	1 day	Wed 10/2/19													First Aid Kit █ 10/2
331	Store Planner Visit	2 days	Tue 10/22/19													Store Planner Visit █ 10/23
332	Purchasing Coordinator Site Visit (Equipment)	2 days	Tue 9/3/19													Purchasing Coordinator Site Visit (Equipment) █ 9/4
333	Purchasing Coordinator Site Visit (Small wares)	2 days	Tue 11/5/19													Purchasing Coordinator Site Visit (Small wares) █ 11/5
334	Construction Complete	0 days	Fri 10/11/19													◆ 10/11
335	Project Complete (Opening Day)	0 days	Fri 11/8/19													◆ 11/8
